

News & Announcements

-Lane Closures on I-240

- **Notice will be given for night time lane closures for installation of glare screen in median**
- Retaining walls along the east and west bound sides are complete.
- Installation of lighting is ongoing.
- Installation of concrete medians and parapet walls continues.
- Paving on the west bound lanes and the collector-distributor road will continue through October.
- All permanent ramps on the east side have been completed and are open.
- The speed limit is **STILL** reduced to **45 mph**. This lowered speed limit applies to the entire project from day one of construction through the completion of the entire project and Memphis Police are onsite to enforce limit.
- Survey crews are working throughout the project. This type of work requires crews to work all over the site and stop to work along the roadway to collect data.
- Crews will be entering and exiting the interstate at all times of the day to work on the construction of this new lane and walls.



News & Announcements

> Phase IV Completion % - 2014

- | | |
|----------------------------------|------------|
| ▪ Glare screen installation | 50% |
| ▪ Complete WB Poplar Ave & Ramps | 80% |
| ▪ Construction of C-D Road 2 | 75% |
| ▪ Complete lighting installation | 70% |
| ▪ Final paving | 25% |



Please visit <http://www.tn.gov/tdot/projects/region4.shtml> for additional project information.

Send email addresses to I-240@SSR-Inc.com for mailing list signup.

Construction News & Schedule



Additional lane, concrete median barrier, collector-distributor road, and retaining wall near Shady Grove overpass.

8/1/14 – 9/1/14

Final paving will begin on EB additional lane, shoulders, and Cd Rd 1. Final striping on the east side will be completed. Interstate lighting on the east side will be operational. Tapered transitions in the concrete median barrier between Cd Rd 1 and additional lane on the east side will be completed. Collection/ Disbursement Road (Cd Rd) 1 will be opened. Construction of sub-grade and base layers of pavement on the west side will continue.

9/1/14 – 10/1/14

Construction of permanent ramps 15A and 15C on the west side at Poplar Ave will begin. Installation of drainage and concrete median on the west side at Walnut Grove will continue. Construction of sub-grade and base layer of pavement will continue. Wiring installation of the west side will continue.

10/1/14 – 11/1/14

Final paving and striping on the west side will wrap up. Installation of roadway signage will finalize. Interstate lighting on the west side will be operational. Final dressing and cleanup will begin.



Construction News & Schedule

For 2014 all construction activity will be focused on finishing the project

- Modify existing median barrier
- Complete ramps at Walnut Grove and Poplar Ave.
- Construction of Collector-Distributor Road
- Lighting and Signage Installation
- Final Paving and Striping



Please visit <http://www.tn.gov/tdot/projects/region4.shtml> for additional project information.

Send email addresses to I-240@SSR-Inc.com for mailing list signup.

Contact Information



- Nichole Lawrence, Region 4 Community Relations Officer
300 Benchmark Place
Jackson, TN 38301
1-731-935-0318
Nichole.Lawrence@tn.gov
- Michael Welch, District Engineer
300 Benchmark Place
Jackson, TN 38301
Michael.Welch@tn.gov




- Patrick Smith, Project Engineer
2650 Thousand Oaks Boulevard,
Suite 3200
Memphis, TN 38118
1-901-683-3900
PSmith@ssr-inc.com
- Mitch Berryman, Site Project Manager
2650 Thousand Oaks Boulevard,
Suite 3200
Memphis, TN 38118
1-901-254-9822
MBerryman@ssr-inc.com
- Alex Ray, Construction Manager
2650 Thousand Oaks Boulevard,
Suite 3200
Memphis, TN 38118
1-901-683-3900
ARay@ssr-inc.com

Construction Information

-Click the following TDOT links for updated lane closures related to the I-240 widening project.

<http://news.tennesseeanytime.org/taxonomy/term/71>

<http://m.tdot.tn.gov/SmartWay/SelectInfo.aspx?Region=4>

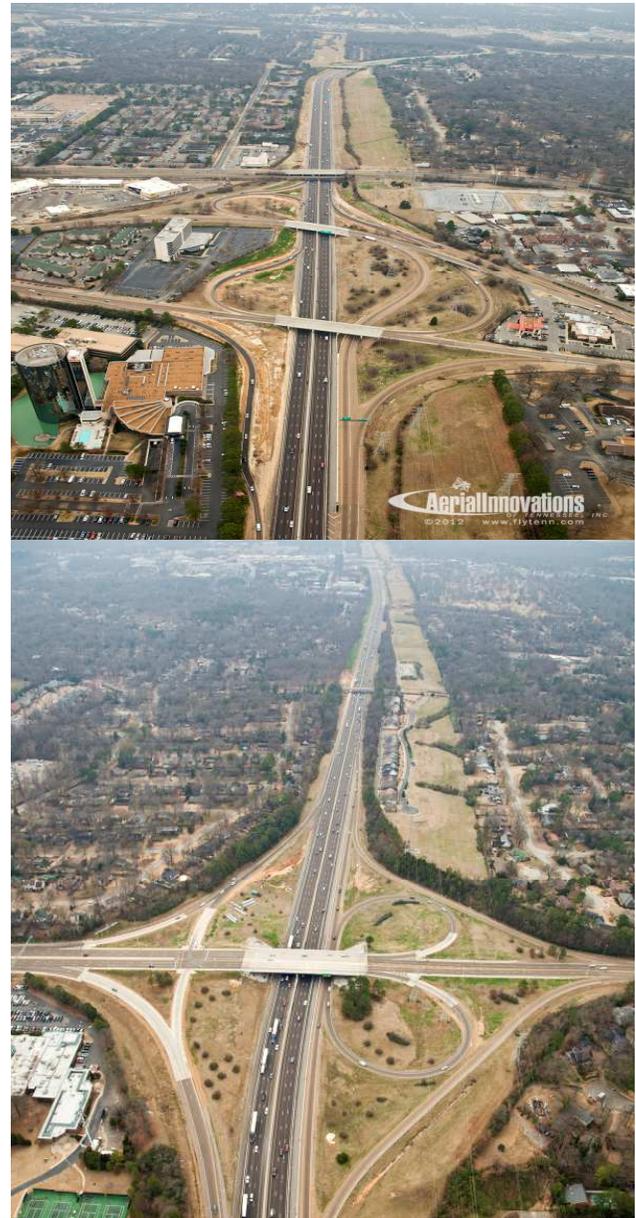

Please visit <http://www.tn.gov/tdot/projects/region4.shtml> for additional project information.

Send email addresses to I-240@SSR-Inc.com for mailing list signup.
